



BA Advisory Desk

Business Analysis Services

SAMPLE DELIVERABLE

Business Case Brief

A decision ready business case that frames the problem, evaluates options, clarifies benefits, identifies risks, and gives leaders a practical recommendation.

CLIENT PRIVACY

Client names and identifying details are anonymized.

DELIVERABLE TYPE

Options analysis, benefits model, risk view, recommendation, and approval brief.

TYPICAL BUYER

Executives, transformation leaders, product leaders, and finance partners.



SITUATION

Leaders needed a decision, not another long discussion.

The team had a strong business problem but weak decision material. Leaders needed options, cost logic, value drivers, implementation risk, and a concise recommendation.

DECISION NEED

Approve, defer, or redesign the investment path.

MAIN RISK

Proceeding without a clear benefits case and adoption plan.

DECISION READINESS



Options, risks, benefits, and implementation path are structured for executive decision making.

OPTIONS ASSESSED

3

Do nothing, targeted improvement, full transformation.

BENEFIT CATEGORIES

6

Speed, quality, cost, risk, service, employee effort.

KEY RISKS

11

Grouped with mitigation and decision impact.

ROADMAP PHASES

4

Sequenced for controlled delivery.

Approve the targeted improvement option. It produces meaningful value, limits delivery risk, and preserves future scale options.



Business case analysis table.

The brief uses structured criteria to compare options in language that executives, finance, and delivery teams can review together.

AREA	FINDING	IMPACT	EVIDENCE NEEDED	RECOMMENDATION
Problem	Manual review creates repeated delays and inconsistent decisions.	Service speed and stakeholder confidence decline.	Baseline cycle time by request type.	Confirm current state metrics.
Option 1	Do nothing keeps spend low but leaves root causes unresolved.	Backlog and frustration continue.	Current rework and escalation cost.	Not recommended.
Option 2	Targeted improvement fixes the highest volume process gaps first.	Fast value with manageable change load.	Volume, pain points, and readiness data.	Recommended.
Option 3	Full transformation offers scale but requires more change capacity.	Higher potential value and higher risk.	Operating model and funding detail.	Defer until foundation is proven.
Benefit	Standardized intake improves completeness and routing.	Reduced rework and fewer escalations.	Before and after completeness rate.	Track monthly.
Benefit	Clear decision rules reduce exception handling.	Better consistency and auditability.	Exception types and repeat causes.	Build rules catalog.
Cost	Implementation requires process design, workflow changes, training, and reporting.	Moderate investment and adoption effort.	Vendor estimate and internal time.	Use phased rollout.
Risk	Stakeholders may resist standardized intake.	Low adoption could reduce value.	User feedback and training needs.	Run pilot with champions.
Risk	Data quality may not support reporting needs.	Benefit tracking may be weak.	Source system data review.	Define metrics early.
Assumption	Leadership can assign a process owner.	Ownership is required for benefit capture.	Named owner and mandate.	Confirm before approval.
Decision	Approve pilot before enterprise rollout.	Limits risk and proves value.	Pilot success criteria.	Approve controlled first phase.

How this creates value


- Gives leaders a clear recommendation.
- Links business pain to benefits and delivery path.
- Separates assumptions from evidence.
- Creates a practical basis for approval.

What this prevents

- Approving spend based on vague urgency.
- Comparing options without common criteria.
- Ignoring change readiness.
- Launching without benefit measures.

Option value and feasibility view.

The options are compared by business value and implementation feasibility to keep the decision practical.

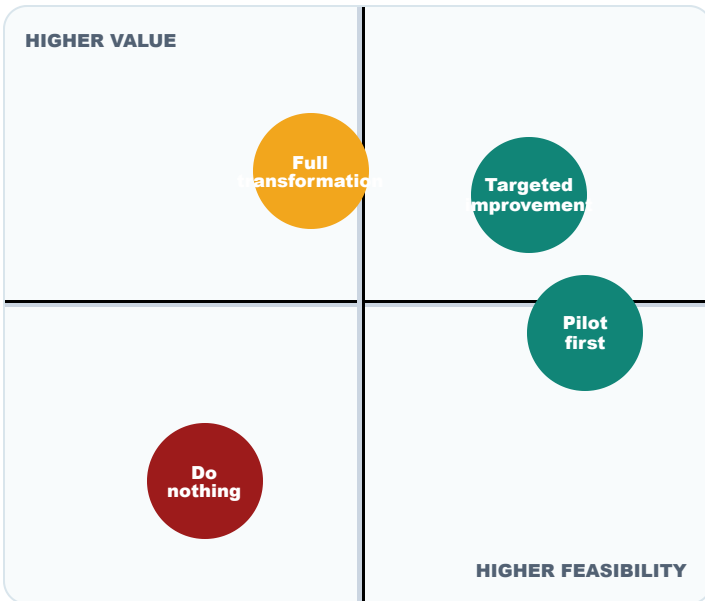

OPTION	VALUE	DELIVERY VIEW
Do nothing	Low	Avoids near term cost but leaves pain unresolved.
Targeted improvement	High	Best balance of value, risk, and speed.
Full transformation	High	Good later option after foundation is proven.
Pilot first	Recommended	Confirms benefits before broader investment.

A strong business case does not just say yes or no. It gives leaders a risk aware path to a better decision.



Risks, assumptions, and mitigation plan.

Each risk is translated into a control or decision so the recommendation stays credible.

RISK	LIKELIHOOD	IMPACT	MITIGATION
Stakeholder adoption is lower than expected.	Medium	Benefits delayed.	Pilot with champions and measure usage.
Process owner is not assigned.	Medium	Decisions drift.	Assign owner before funding release.
Source data is incomplete.	High	Weak benefit tracking.	Define minimum data set.
Training effort is underestimated.	Medium	Poor rollout experience.	Create quick reference material.
Vendor estimate expands.	Medium	Budget pressure.	Use fixed scope first phase.
Leadership requests broader scope too soon.	Medium	Risk increases.	Use phase gate approval.

Approval conditions

- Named owner
- Pilot scope
- Success measures

Finance checks

- Cost range
- Benefit owner
- Tracking method

Delivery checks

- Resource plan
- Change plan
- Risk controls



Business case approval roadmap.

PHASE 1

Confirm evidence

- Baseline metrics
- Pain point validation
- Owner assigned

PHASE 2

Approve pilot

- Scope first wave
- Set budget guardrail
- Define success

PHASE 3

Deliver and measure

- Implement process changes
- Track adoption
- Review benefits

PHASE 4

Scale decision

- Compare results
- Approve scale
- Close gaps

Decision log

DECISION	RECOMMENDATION	STATUS
Recommended option	Approve targeted improvement.	Approve
Funding release	Release pilot funding first.	Controlled
Scale	Decide after benefit review.	Hold
Ownership	Assign process owner before start.	Required

Open questions

- What baseline metric will define success?
- Who owns benefit tracking?
- What scope must stay out of phase one?
- What decision date is needed?

The package converts a broad investment discussion into a decision ready brief with evidence, options, and a controlled path forward.
